



# APPLIED RESEARCH BUILDING

DATE: **7/26/21 - 7/30/21**

PHASE: **Building Pad Prep**



Building Pad and Earthwork Complete,  
Ready for Drilling Activities!



McCarthy + SmithGroup  
ARB Design Build Team



# APPLIED RESEARCH BUILDING

DATE: 7/26/21 - 7/30/21

PHASE: Caisson Prep

Rebar Tied for  
Caissons - 55 in  
Total!




Caissons Tied,  
Inspected, and  
Ready to be  
Placed



# APPLIED RESEARCH BUILDING

DATE: 7/26/21 - 7/30/21

PHASE: **Helen Site Utilities**

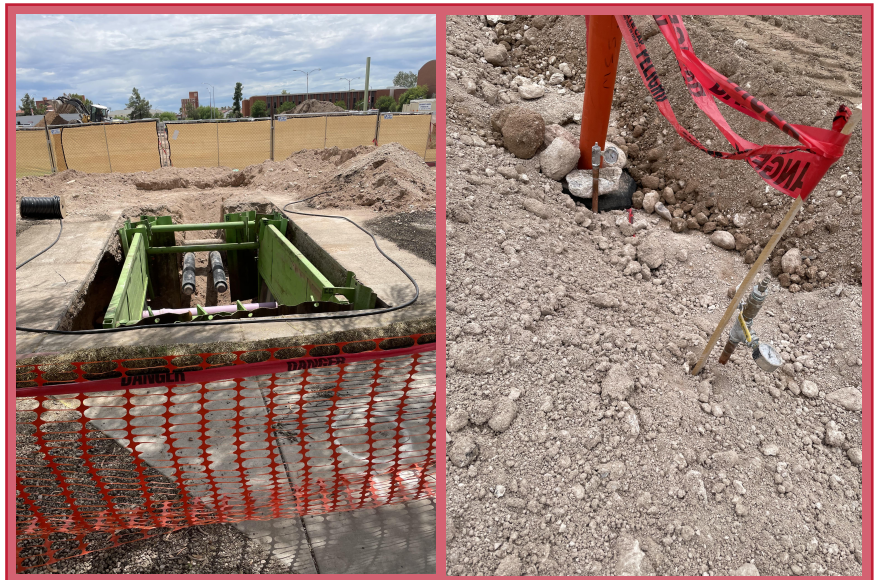

Site Utility Backfill and Tie In's



Helen Street  
Communications  
and Sewer  
Installation



# APPLIED RESEARCH BUILDING

DATE: 7/26/21 - 7/30/21

PHASE: Highland Walkway & Temp Drain route

Highland Walkway  
Fencing and Final  
Finishes



Retention wall  
drainage route  
poured





## APPLIED RESEARCH BUILDING

DATE: **7/26/21 - 7/30/21**

PHASE: **What's next?!**

**COMING  
SOON!**

- Drilling and Placing Caissons to Support the Foundation System
- Tower Crane Base and Anchor Bolts
- Helen Street Site Utility completion
- Highland Walkway Re-Opening
- Concrete Cast In Place Structure



McCarthy + SmithGroup  
ARB Design Build Team
