

DATE: **08/08/22 - 08/19/22** 

PHASE: Project Overview



**Facing North View** 







DATE: **08/08/22 - 08/19/22** 

PHASE: Parking Lot 2021 Reopening



Grading Complete - Asphalt on the way!



Striped and ready for reopening!

### Parking Lot 2021:


Re-paved, re-striped and open for parking starting Monday 8/22/22!





DATE: **08/08/22 - 08/19/22** 

PHASE: Level 4 Mechanical Room Work

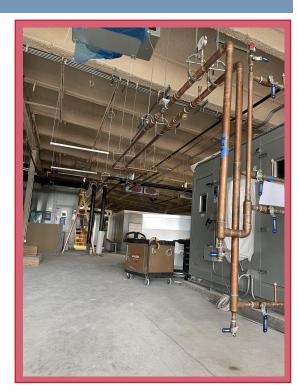



Plumbing on the west side is complete. A mobile crane was mobilized and multiple trucks of main ductwork were flown into the space. The construction team of over 40+ are hard at work installing all the new materials!







DATE: **08/08/22 - 08/19/22** 

PHASE: Highland Corridor



Crews Setting Asphalt with Paving Machine



#### **Highland Corridor:**

After a summer of closure, the Highland pathway is open and ready for public use! McCarthy remains hard at work for the full completion of the Highland Corridor realignment, January 2023!





DATE: **08/08/22 - 08/19/22** 

PHASE: Stair #3

After the guardrail is complete, illuminated glass will be installed inside the steel frames for a unique architectural/industrial finish





Stair #3 at SE Corner Guardrail

#### Fun Fact:

The rustications on the concrete wall (behind the stair) stop and start on a parallel slope to the rise of the stair. This was an extremely challenging coordination item for the design-build team, but the final look is unbeatable!






DATE: **08/08/22 - 08/19/22** 


PHASE: Metal Panel Facade



West side exterior in progress



The white plastic temporarily protects the metal panel system during construction.

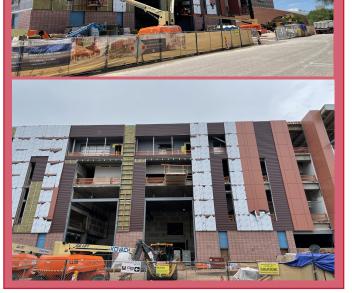

North side in progress





DATE: **08/08/22 - 08/19/22** 

PHASE: What's next?!?



- East side metal panel facade
- Exterior Glass installation



