

DATE: 09/19/22 - 10/03/22

PHASE: Project Overview



Facing North View





Facing South View



DATE: 09/19/22 - 10/03/22


PHASE: Elevator Cab Buildout

Fun Fact:

Elevator installation is a rigorous process. Fabrication of the elevator cabs began in June 2021 and the installation of the elevator shaft started nearly a year later. The delivery of the elevator cabs are tracking for the end of October.











DATE: 09/19/22 - 10/03/22

PHASE: North Yard & Concrete

The yard north of the building will be used for deliveries and to stage special equipment before it is tested inside the building. Landscaping and colored concrete will be added after the exterior panels have been installed.



Irrigation sleeves for the landscape







DATE: 09/19/22 - 10/03/22

PHASE: Bathroom Tile



Tile in west restrooms on level 1 and 2 are complete! Awaiting shower tile for the restrooms with showers.








DATE: 09/19/22 - 10/03/22

PHASE: Glass Installation

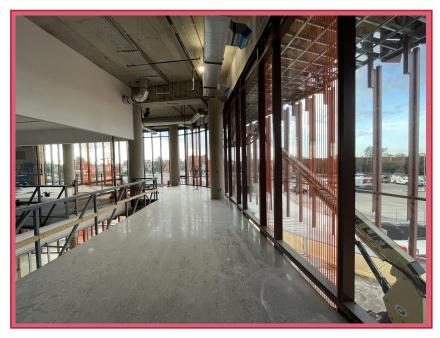

Interior View from level 2 facing SW





The storefront on the southwest corner is nearly complete! Glass has been set on level 3, and the glass crew has moved to the north side.



DATE: 09/19/22 - 10/03/22

PHASE: Glass Installation











DATE: 09/19/22 - 10/03/22

PHASE: Metal Panel Facade



Metal panel on South side



Installing green girts and insulation





DATE: 09/19/22 - 10/03/22

PHASE: What's next?!?



- North Yard Gates

- Exterior Glass Installation

- Interior Glass Installation

- Lab Cranes

- Highland Path Sub Grade

