


Chemistry Building Renovation



Construction Update – Week of February 14th, 2022

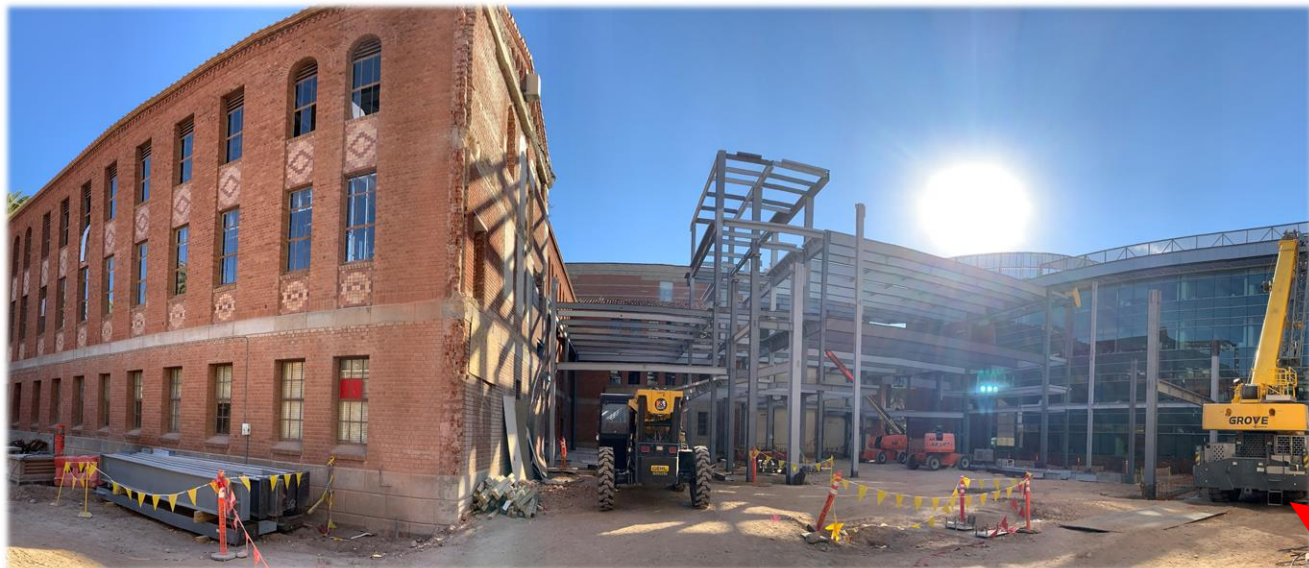

Structural steel is complete on the east side of the new building - **“The Commons”**. Stay tuned for the west side to be complete and steel deck to be set in place.

Architectural Rendering




Chemistry Building Renovation

Construction Update – Week of February 14th, 2022



Level 2: Overhead HVAC is in; Fire protection piping is in, and walls are starting to be insulated and closed-up.

Level 3: Follows behind level 2 with framing and plumbing.

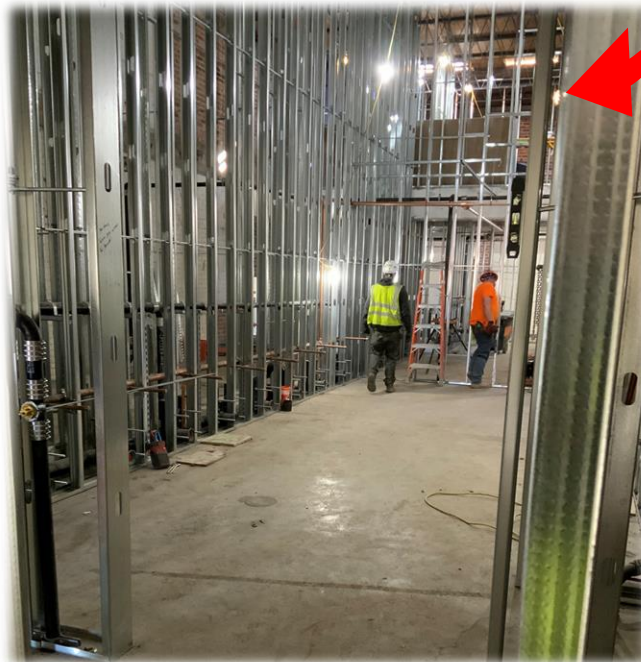

Level 1: With the occupants in their new space on the east side of the existing building, prep for demo has begun on the west side. This will soon be the location for a new elevator!

